

# AIR CONDITIONING JOBSITE STARTUP SHEET

## Owner

Name: \_\_\_\_\_

Phone Number: \_\_\_\_\_

## Contractor

Company: \_\_\_\_\_

Name: \_\_\_\_\_

Phone Number: \_\_\_\_\_

## Equipment Information:

Outdoor Unit Model #: \_\_\_\_\_

Serial #: \_\_\_\_\_

Install Date: \_\_\_\_\_

Evaporator Model #: \_\_\_\_\_

Serial #: \_\_\_\_\_

Install Date: \_\_\_\_\_

Indoor Unit Model #: \_\_\_\_\_

Serial #: \_\_\_\_\_

Install Date: \_\_\_\_\_


Furnace/ Air  
Handler \_\_\_\_\_  
CFM

Super Heat = \_\_\_\_\_ °F

Sub Cooling = \_\_\_\_\_ °F

Notes:

Supply Air DB: \_\_\_\_\_ °F  
WB: \_\_\_\_\_ °F

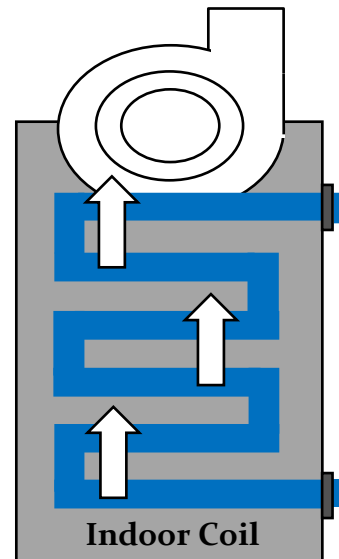


Return Air DB: \_\_\_\_\_ °F  
WB: \_\_\_\_\_ °F

\_\_\_\_\_ °F

\_\_\_\_\_ °F

\_\_\_\_\_ °F


\_\_\_\_\_ °F



Liquid Line (High Side)

Outside Temperature \_\_\_\_\_ °F

Vapor Line (Low Side)

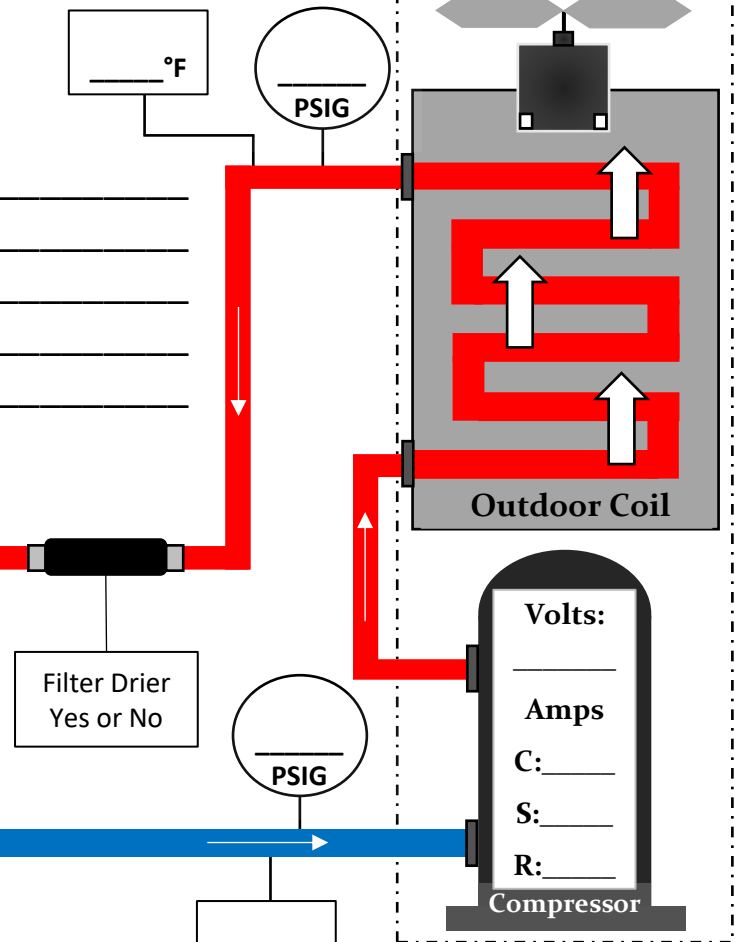

Outdoor Coil

Volts: \_\_\_\_\_

Amps \_\_\_\_\_

C: \_\_\_\_\_

S: \_\_\_\_\_

R: \_\_\_\_\_

Compressor
